
ENVISION

Development


Recapitalization and Construction

Aug 12, 2019



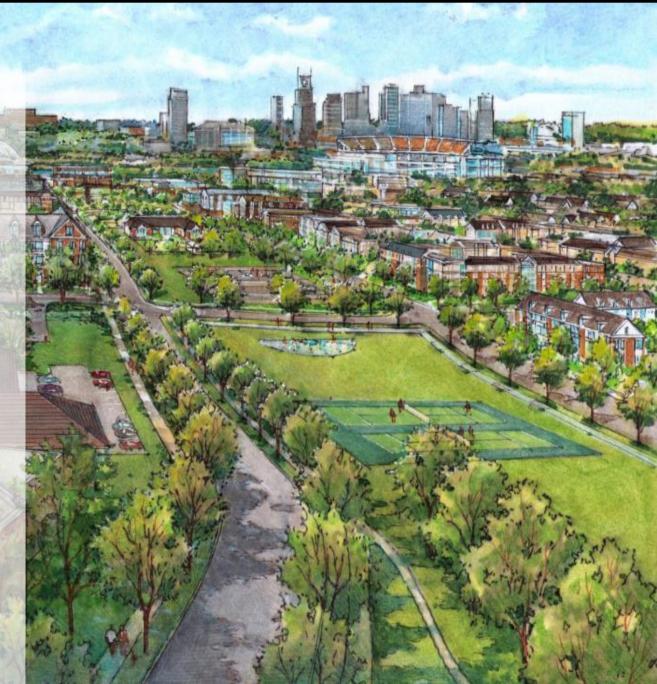

ENVISION LEGACY PROPERTIES

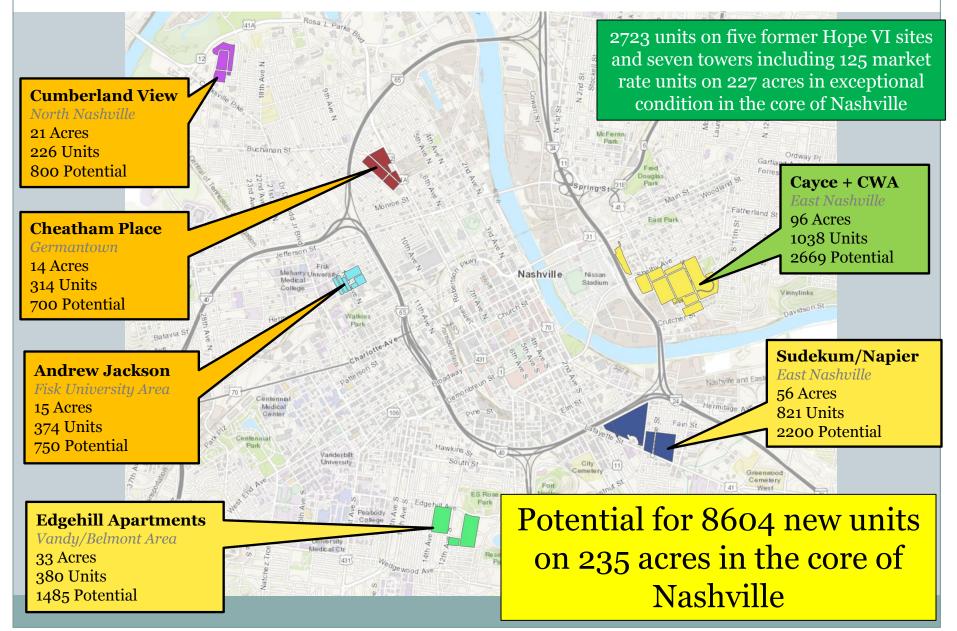


ENVISION PROCESS




Existing Conditions

What is the ground truth and what are the needs



Options and Alternatives

What are the wants and how do we address gaps in needs and services



Preferred Plan

Finalizing the plan and determining how to achieve it



Implementation

Work collaboratively with residents and other stakeholders to enact the plan



ENVISION CAYCE

Proposed development:

• Envision Cayce replaces our current subsidized public housing with new affordable housing and market rate units.

• Plan Highlights:

- Current units = 1,038
- Envision Cayce Target units = 2,700
- Total Units increased by = 1,662
- 40 / 15 / 45

• Early Successes:

- Barret Manor Completed
- Kirkpatrick Park Construction
- Boscobel I Under Construction
- Boscobel II Under Construction
- Boscobel III Under Construction
- Boscobel IIIa (Townhomes) Design
- Boscobel IV Design
- Explore School Under Construction



Moving forward:

• Create and implement the People and Neighborhood Plan

Envision Napier Sudekum

- 2016 Choice Neighborhoods Planning Grant (\$500,000)
- Planning began in November 2016, and HUD accepted the plan in August 2018
- Active planning included over 60 community meetings, design charrettes, and community engagement events
- The Plan is currently going through the zoning approval process:
 - Planning Commission Approval
 - Introduced at Metro Council (1st Reading)
 - Public Hearing at Metro Council (2nd Reading)
 - Final Hearing at Metro Council (3rd Reading)
 - Bill becomes effective

5/23/2019 7/02/2019 8/06/2019 8/20/2019 9/03/2019



Residents and community members at the Metro Council Public Hearing on August 6, 2019



Envision Napier and Sudekum

Proposed development:

- Up to 2,100 at 40-20-40 mix
- Up to 150,000 sq. ft. commercial space

Plan Highlights:

- New 4 acre park
 Comprehensive Early Learning Center
- Grocery Store
- Regional Community Center

Moving Forward:

- Evaluate
 establishing a
 Redevelopment
 District
- Select Phase I project to continue momentum and engagement



Envision Edgehill Apartments

- Funded with Metro CIB
- Planning began in August 2018, and now is wrapping up
- Active planning included over 55 community meetings, design charrettes, and community engagement events, and over 1,800 participant touches
- Envision Edgehill Apartments Next Steps:
 - Kick off rezoning process
 - Rezoning process complete

August 2019 Early 2020



Envision Edgehill Apartments

Final Concept Plan

Supports:

- 1,400 1,500 residential units
- 160,000 sf of Commercial/nonhousing
- ~12% open space





Envision Cumberland View Apartments

Existing Conditions

- Construction was completed on the property in February 1969
- 21 acres
- 226 units
 - 1 BR: 24
 - 2 BR: 96
 - 3 BR: 50
 - 4 BR: 28
 - 5 BR: 24
 - 6 BR: 4





KIRKPATRICK PARK APARTMENTS

Architect Smith Gee Studios

<u>Contractor</u> RG Anderson Company

Key Milestones Close HUD Loan: 11/27/17 Project Ground Breaking: 11/29/17 Phase 1 Occupancy: 4/11/19 Phase 2 Occupancy: 5/30/19 Phase 3 Occupancy: 6/27/19 Bldgs. A&B Occupancy: 7/25/19 HUD Final Inspection: 9/26/19

<u>Budget</u>

\$26,008,899 99% Complete

Building Size(s): 92,466 SF Site Size: 3.75 Acres

- 1-3 Story Units/Townhomes
- 94 Total Units
- Utilizing HUD 221(d)4 Loan, Metro CIB and HOME Funds



CURRENT PROGRESS: KIRKPATRICK PARK



EXPLORE SCHOOL

<u>Architect</u> Johnson Johnson Crabtree and Assoc.

 $\frac{Contractor}{RG\,Anderson}$

<u>Key Milestones</u> Substantial Completion Elementary 8/2/19 Ribbon Cutting 8/2/19 Substantial Completion Middle 10/18/19

<u>Budget</u>

\$30,400,000 69% Complete

Building Size: 85,858 SF Site Size: 4.69 Acres

- Grades K-8 with 4 classrooms per grade
- 3 Story Building
- Classrooms for science, language, music, and life skills
- Opening Fall 2019
- Utilizing New Market Tax Credits



CURRENT PROGRESS: EXPLORE SCHOOL



BOSCOBEL I: Davidson Apartments

<u>Architect</u> Kline Swinney Associates

Contractor Hardaway Construction

Key Milestones Ground Breaking: 5/10/18 Demo Completed: 4/17/18 Full GC NTP: 8/16/18 Tenant Occupancy: 1/20/20

Budget \$27,376,661.00 60% Complete

Building Size: 146,019 SF Site Size: 1.549 Acres

- 96 units
 - 50 PBRA

 - 24 Workforce 22 Market Rate
- Available Winter 2020
- LIHTC, CITC, and Market Rate Loan
- **Received NHTF Grant**



CURRENT PROGRESS: BOSCOBEL I - Davidson Apartments



BOSCOBEL II: Minnick Place

17

<u>Architect</u> Kline Swinney Associates

Contractor Hardaway Construction

<u>Key Milestones</u> Groundbreaking: Fall, 2018 Demo Completed: 9/15/18 Tenant Occupancy: 6/18/20 - Townhome: 12/26/2019 - Bldg. C: 5/5/20 - Bldg. D: 6/18/20

Budget \$34,228,806.00 44% Complete

Building Size: 153,493SF Site Size: 5.78 Acres

- 101 units
 - 45 PBRA

 - 15 Workforce 41 Market Rate
- Available Summer 2020
- LIHTC, CITC, Market Rate Loan, and HOME Funds



CURRENT PROGRESS: Boscobel II - Minnick Place



BOSCOBEL III: Red Oak Flats

Architect EOA

<u>Contractor</u> RG Anderson Co.

Key Milestones

Close Loan: 8/9/2019 Ground Breaking: 8/20/2019 Occupancy: 1/13/2021

<u>Budget</u> \$34,417,437.00 1% Complete

Building Size: 109,136 SF Site Size: 2.89 Acres

- 4-Story Apts w/ parking under
- 102 Total Units
 - 45 PBRA
 - 15 Workforce
 - 42 Market Rate
- Available Winter 2021
- LIHTC, CITC, Market Rate Loan, and HOME Funds





7th and Dew Street Corner Perspective

CURRENT PROGRESS: Boscobel III - Red Oak Flats



BOSCOBEL IIIA: Red Oak Townhomes

Architect EOA Architects

Contractor TBD CM@R

Key Milestones CM On Board: 10/15/2019 100%CD: 3/1/2020 GMP: 4/1/2020 MDHA Board: 4/14/2020 Building Permits/Loan Close/NTP: 5/1/2020 Groundbreaking:

Budget Rough Estimate: \$15.5M 0% Complete

Building Size: ~55,000 SF Site Size: ~2.8Acres

- 40 units
 - 25 PBRA
 - 7 Workforce 8 Market Rate
- Available Fall 2022
- Funding TBD



Community Campus: Community Center / Library

Architect

 $\underline{Contractor}_{American}$

Key Milestones

DDs: 10/1/2019 CDs 100%: 3/2/2020 Permits/Loan Close: 4/27/20 MDHA Approves: 5/12/2020 Completion: 10/1/21

Budget

\$30,000,000.00 0% Complete

Building Size: 60,000 sq.ft Library; 25,000 sq.ft Center; 35,000 Site Size: ~1.1Acres

- Available Fall 2021
- 2020 NMTC
- In Opportunity Zone
- Metro Support; Metro Library; and Metro Gov't support reqd



Boscobel IV

23

Architect Smith Gee Studios

Contractor TBD CM@R

Key Milestones Master Plan: 8/16/2019 9% LIHTC Award: 8/31/2019 CM on Board: 10/15/2019 100% CD: 4/1/2020 Full Building Permits/Close Loan/NTP: 6/1/2020 Groundbreaking:

Budget

~\$50,000,000.00 0% Complete

Building Size: ~220,000 SF Site Size: ~3.3 Acres

Units: 164_

- 72 PBRA
- 28 Workforce
- 64 Market Rate
- Structured Garage
- Available Fall 2021

Funding

- 2019 9% LIHTC Building B
- 2020 4% LIHTC Building A



BORDEAUX : HARPER COVE FLATS

Architect EOA

<u>Contractor</u> RG Anderson

Location: Hospital Lane in Northwest Nashville

<u>Key Milestones</u> Construction Complete: 10/22/19 Construction 70% Complete

Projected Funding \$9,325,869 Total Cost \$3,925,869 HUD DRG \$5,400,000 Bank Financing

Building Areas: Four (4), three (3) story buildings with a total combined area of 52,227 SF

Building 1 16,034 SF Building 2 13,284 SF Building 3 10,181 SF Building 4 12,768 SF Surface Parking Site Size: 5 Acres

40 Workforce Apartments



CURRENT PROGRESS: HARPER COVE FLATS



25

Curb Victory Hall Public Private Partnership

Private Partners Giarratana, LLC

Donor Mike Curb

Architect ESA

Contractor **RG** Anderson

Location: 1117 12th Avenue South

Key Milestones

Construction Loan Closed: 8/6/19 Construction Complete: 7/20 Construction 3% Complete

\$8,051,342 Projected Funding Total Cost 9% LIHTC Equity CITC Loan \$6,510,037 541,305 500,000 Curb Donation 500,000 THTF Grant

Building Areas:

Residential 20,429 SF 4,894 SF Parking Garage

- 4 Stories with Parking Garage
- 39 apartments (37 Veteran units, 2 market units)
 - Studio:
 - 1-BR:
 - 2-BR:
- Community room with computer and exercise areas



Randee Rogers Apartments

<u>Architect</u> Kline Swinney Associates

Contractor To Be Determined

Location: 1419 Rosa L. Parks Boulevard

Key Milestones

Advertise for Demo Bids:	8/	15/19
Receive Demo Bids:	8,	29/19
Demo NTP (Pending ER):	10	0/1/19
Demo Complete:	12	/1/19
Advertise Building:	9/	19/19
Receive Building Bids:		22/19
Building NTP:		18/19
Construction Complete:	2	/21

Projected Funding \$28,000,000 Total Cost Utilizing Metro CIB, 4% LITHC and Conventional Bank Loan

Building Areas: Residential 118,039 SF Parking Garage 47,434 SF Site Size: 1.76 Acres

- 4 Stories with Parking Garage
- 100 Apartments
- Income Levels
 - Sec 9:
 - Workforce:

50 25 25

Market:



27

New Central Maintenance Facility

<u>Architect</u> Barge Cauthen & Associates

> <u>Contractor</u> To Be Determined


Location: 410 Marina Street, Levy Place

Key Milestones

Advertise Mass Grading:8/16/19Receive Grading Bids:9/17/19Mass Grading NTP:10/1/19Advertise Building:10/8/19Receive Building Bids:10/30/19Building NTP:12/3/19Construction Complete:6/1/20

Projected Funding \$2,500,000 Total Cost \$2,500,000 Unrestricted Funds

• 18,120 SF building to house Central Maintenance crews along with surface parking for MDHA maintenance vehicles

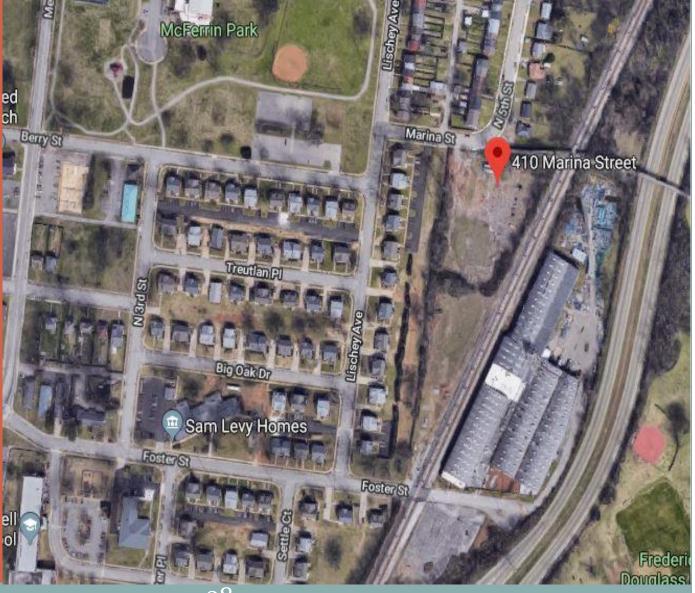

Trolley Barns Parking Garage

<u>Architect</u> To Be Determined

<u>Contractor</u> To Be Determined

Location: Rolling Mill Hill

Key Milestones Designer Interviews: 8/7/19 and 8/8/19 Prepare Design/Construction Documents: 8/19/19 Thru 3/31/20 Building NTP: 6/1/20 Construction Complete: 5/1/21

<u>Projected Funding</u> \$12,700,000 Total Cost Financing to be determined

• +/- 400 parking spaces

- Trolley Barns:
- Ryman Lofts:
- Existing Displaced Parking Site:
- Vehicle connection to existing Ryman Lofts surface parking/access drive
- Possible pedestrian connection to greenway ramp_______
- Provisions to separate Trolley Barns and Ryman Lofts parking



Permanent Supportive Housing

Design/Build Team To Be Determined

Location: 505 2nd Avenue North


Key Milestones

Eval. Comm. Rec.:	8/15/19
Begin Pre-Con Services:	9/1/15
Submit for Permit:	12/20/19
CM Mobilize:	2/15/20
Issue Permits:	2/21/20
Begin Site Work:	2/24/20
CM Submit GMP:	3/17/19
Begin Bldg. Const.	4/4/20
Construction Complete:	5/27/21

Projected Funding \$24,000,000 Total Cost \$24,000,000 Metro CSP Funding

Building Areas: Residential: +/-100,000 SF Site Size: 0.2 Acres

- Proposed 12 Stories
- Floors 1 and 2 will consist of offices and support space for Metro Homeless Impact Division
- Floors 3 thru 12 will have 100+ 350+/- SF one bedroom apartments and support space with separate 1st floor entrance

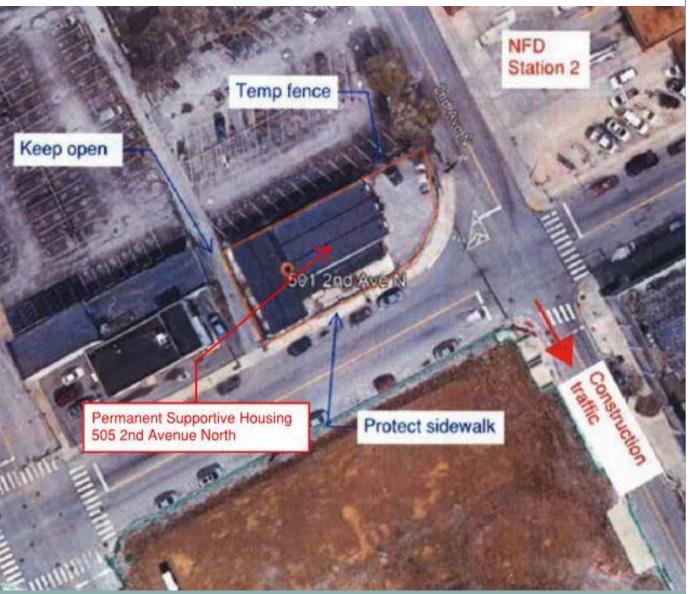

PUBLIC PRIVATE DEVELOPMENT



PUBLIC PRIVATE DEVELOPMENT (Cont.)

View from Shelby Avenue and 4th Street



Additional Projects in Concept Phase

<u>2020</u>

- Edgehill I 264 Mixed/Income and 20,000 sf Mixed Use
- Marathon Village Innovative 9% LIHTC: 140 Mixed Income/ Mixed Use Units
- Boscobel Storm Water/ Sewer Separation to support east Boscobel Unrestricted Funds

<u>2021</u>

- Napier I 9% + 4% LIHTCs (2020 Award): Approx. 152 Mixed Income Units
- Boscobel Central Park
- Boscobel Storm Water to Cumberland TIF

<u>2022</u>

• Boscobel V - 9% + 4% LIHTCs (2020 Award): Approx. 152 Mixed Income Units

RECAP WORK LOAD

<u>August 2018</u>:

- KP
- Explore
- Boscobel I
- Boscobel II

August 2019 (Completion date):

- KP (Sep 19)
- Explore (Dec 19)
- Boscobel I (Dec 19)
- Boscobel II (Jun 20)
- Boscobel III (Dec 20)
- Boscobel IIIA (Jun 21)
- Center/Library (Oct 21)
- Boscobel IV (Dec 21)

CONSTRUCTION WORK LOAD

<u>August 2018</u>:

- Bordeaux Townhouses
- Affordable Housing Projects
- Community Development Projects
- Davis-Bacon Monitoring
- Procurement/DBE

<u>August 2019 (Completion):</u>

- Bordeaux Townhouses (Oct 19)
- Curb Victory Hall (Jul 20)
- Randee Rogers (Feb 21)
- Maintenance Facility (Jun 20)
- Trolley Barns Parking Garage (May 21)
- Supportive Housing (May 21)
- Marathon Village (Dec 21)
- Affordable Housing Projects
- Community Development
 Projects
- Davis-Bacon Monitoring
- Procurement/DBE

Diversity Business Enterprise (DBE)

YEAR	NON DIVERSITY AWARDED	NON DIVERSITY AWARDED %	MBE AWARDED *	MBE AWARDED %	WBE AWARDED	WBE DOLLARS AWARDED %	SMALL BUSINESS AWARDED	SMALL BUSINESS AWARDED %	TOTAL DBE AWARDED	TOTAL DBE AWARDED %
2014	\$7,229,528	65.41%	\$1,871,332	16.93%	\$713,206	6.45%	\$1,238,324	11.20%	\$3,822,862	34.59%
2015	\$14,054,985	78.55%	\$3,289,535	18.38%	\$7,035	0.04%	\$541,825	3.03%	\$3,838,395	21.45%
2016	\$27,636,491	78.41%	\$2,656,005	7.54%	\$3,632,577	10.31%	\$1,319,535	3.74%	\$7,608,117	21.59%
2017	\$19,635,521	67.18%	\$4,632,315	15.85%	\$4,371,980	14.96%	\$588,924	2.01%	\$9,593,219	32.82%
2018	\$20,940,477	50.50%	\$8,269,290	19.94%	\$6,494,721	15.66%	\$5,758,803	13.89%	\$20,522,814	49.50%
Q1 2019	\$3,371,911	66.80%	\$1,058,484	20.97%	\$64,780	1.28%	\$552,926	10.95%	\$1,676,190	33.20%
Totals	\$89,497,002	65.54%	\$21,776,961	15.95%	\$15,284,299	11.19%	\$10,000,337	7.32%	\$47,061,597	34.46%

* MBE- includes African Americans, Native Americans, Hispanic Americans, Asian Pacific Americans, Hasidic Jews

This summary sheet does not incorporate the CD's department DBE report since they report separately from construction & procurement.
